



# Arlington High School Building Project

AHS Construction Update – 9/1/2022

## Arlington HS Construction Schedule: April 2020 – April 2025

### Construction Details


Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. For Phase 1, only final testing and landscape work remains. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

### COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates  
<https://ahsbuilding.org/news/construction-updates/>  
 For more information, visit:  
[www.ahsbuilding.org](http://www.ahsbuilding.org)  
 Email questions or concerns to:  
[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative,  
 (617) 352-8593

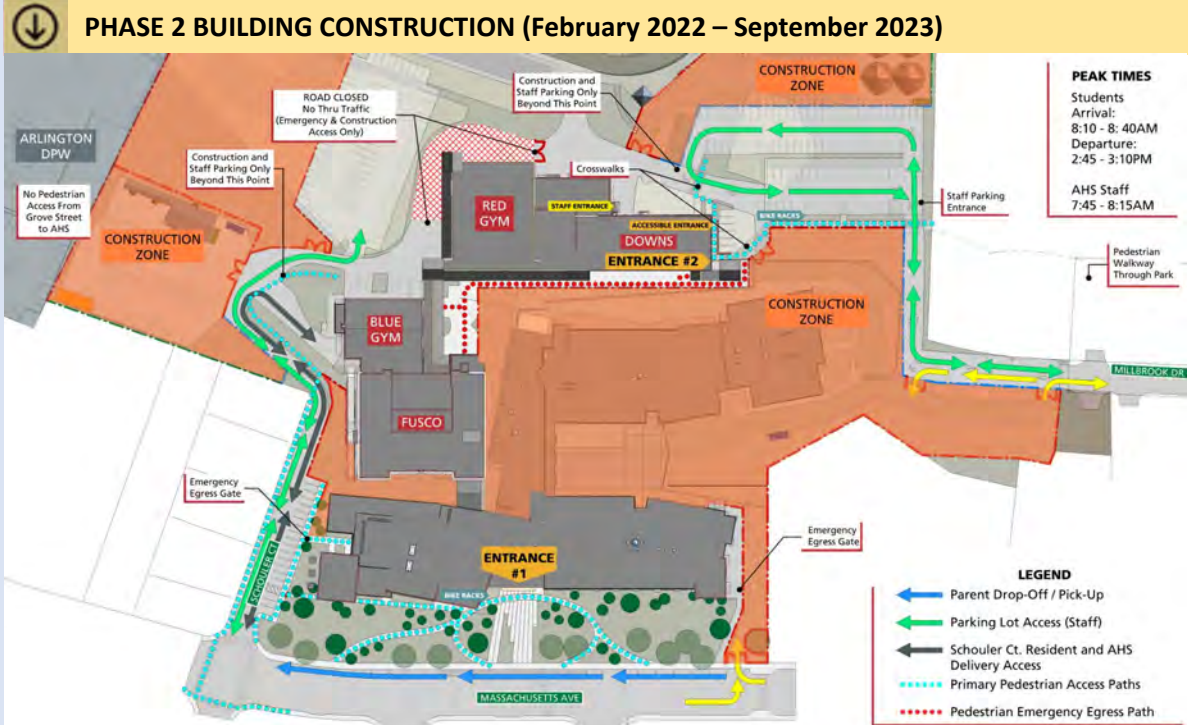

### Construction Look Ahead – Week of September 5<sup>th</sup>, 2022

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts:

- Deliveries/demo debris trucking ongoing
- Mass Ave access to Main Entrance #1 now open
- Schouler Court sidewalk and parking now open
- **Mass Ave water line tie-in scheduled for 9/7 thru 9/9, 8 PM – 5 AM. Work to be performed on night shift. Two-way traffic will be maintained at all times.**

#### General Site Activities:

- Phase 2:
  - Underground utilities and foundations ongoing
  - Debris trucking thru Mill Brook Drive
  - Dust mitigation ongoing
  - Steel and concrete deliveries
- Phase 1 Building Closeout:
  - Temporary rope fence installed to protect grass growth
- West Parking Lot (adjacent to DPW):
  - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
  - Contractor storage and parking
- Schouler Court:
  - Construction vehicles entering and exiting project site

#### Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future





CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF SEPTEMBER 5<sup>TH</sup>, 2022

#### Progress Photographs – Taken Week of 8/29/2022



*Photograph 1: Phase 2 Foundations Progress*



*Photograph 2: Building D/E South Elevation (Main Entrance #1)*





CONSIGLI  
Est. 1905

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF SEPTEMBER 5<sup>TH</sup>, 2022



*Photograph 3: Building E West Elevation (Schouler Court)*



*Photograph 4: D Building Southeast Elevation (Mass Ave)*





CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF SEPTEMBER 5<sup>TH</sup>, 2022



*Photograph 5: Phase 2 East Elevation (Mill Brook Drive)*
